


HCPS PROJECT PROGRESS REPORT

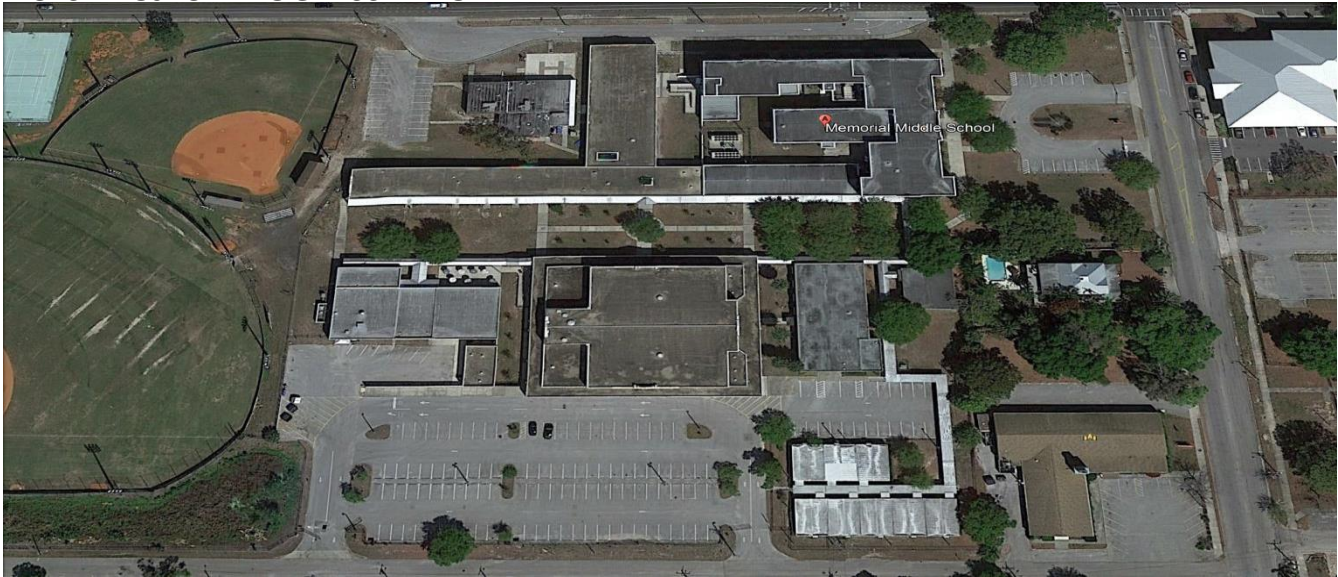

PROJECT INFORMATION: Before During After

Name: Memorial Middle School
Address: 4702 N. Central Avenue
City/State/Zip: Tampa, FL 33603
 District Project Number: **100081**

PROJECT OVERVIEW: (A=Actual, P=Projected) Date (A/P)

Project Start:	TBD	
Inspection/Task:	TBD	
Inspection/Task:	TBD	
Inspection/Task:	TBD	
Inspection/Task:	TBD	
Inspection/Task:	TBD	
Final Completion:		
Total Project Duration:	TBD	Days

ADMINISTRATIVE OVERVIEW:

Total # of Bid-Vendors: TBD

of OSD/MBE/SBE Bid-Vendors:

of Local Bid-Vendors:

\$ Value of OSD/MBE/SBE Participation: \$ -

\$ Value of Local Participation:

OSD/MBE/SBE PARTICIPATION REGISTRATION:

OSD/HCPS
 State of Florida
 County List:
 City List:
 Other List:

PROGRESS PENDING ISSUES (& RESPONSIBILITIES):

Current Critical Issues:

Issue	Responsibility

COMMENTS:

PROJECT DIRECTORY:

HCPS Department: Facilities Maintenance Support
HCPS Representative: Ben Moore

Contractor / Bid-Vendor: TBD
Contractor / Bid-Vendor: TBD
Contractor / Bid-Vendor: TBD
Contractor / Bid-Vendor: TBD
Contractor / Bid-Vendor: TBD

Construction Manager / GC: N/A
 CM/GC PROJECT MANAGER:

Design Professional: CB Goldsmith & Associates

REPORT DATE, PREPARED BY: 4/30/2019 Stephen Ellis

PROJECT DESCRIPTION:

Scope of Work:
 Partial Roof Replacement

CONSTRUCTION UPDATE:

TYPE	% COMP.	REMARKS
Site Visit	5%	
Design Phase	20%	
Bid Posting/Award	0%	
Board Approval	0%	
Tear-Off	0%	
Dry-In	0%	
Cap Sheet	0%	
Sheet Metal	0%	
Sub Completion	0%	
Project Closeout	0%	

CONTRACT STATUS:

CURRENT CONTRACT AMOUNT: \$ 1,138,276.00
AMOUNT BILLED TO DATE: \$ -
PERCENT DOLLARS EXPENDED:
CONTRACT CALENDAR DAYS: TBD
CALENDAR DAYS EXPENDED:
PERCENT TIME EXPENDED:
TOTAL LOST WEATHER DAYS:
