


# HCPS PROJECT PROGRESS REPORT

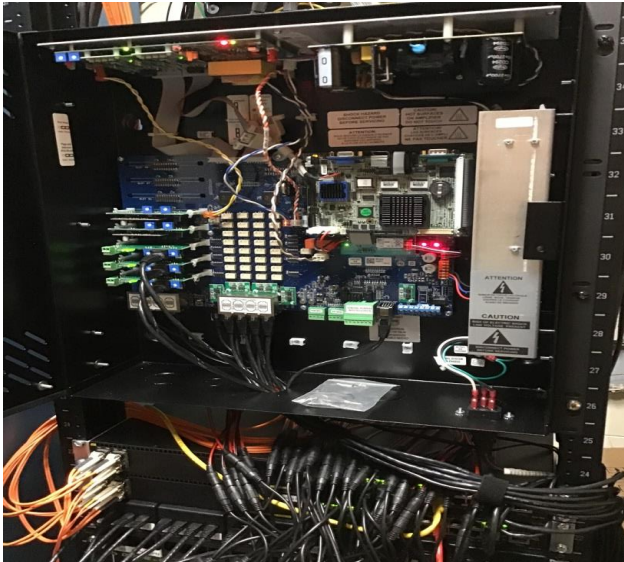

**PROJECT INFORMATION:**  Before  During  After

**Name:** Ferrell Magnet / Intercom Replacement Project  
**Address:** 4302 24th Street  
**City/State/Zip:** Tampa, Florida 33610  
 District Project Number: 100059

**PROJECT OVERVIEW:** (A=Actual, P=Projected)

	Date	(A/P)
<b>Project Start:</b>	01/09/19	A
<b>Inspection/Task:</b> System Test	04/01/19	A
<b>Inspection/Task:</b>	N/A	P
<b>Inspection/Task:</b>	N/A	P
<b>Inspection/Task:</b>	N/A	P
<b>Inspection/Task:</b>	N/A	P
<b>Final Completion:</b>	04/01/19	A
<b>Total Project Duration:</b>	59 Bus Days	

**ADMINISTRATIVE OVERVIEW:**

<b>Total # of Bid-Vendors:</b>	1
<b># of OSD/MBE/SBE Bid-Vendors:</b>	0
<b># of Local Bid-Vendors:</b>	1
<b>\$ Value of OSD/MBE/SBE Participation:</b>	\$ -
<b>\$ Value of Local Participation:</b>	\$ 140,066.00

**OSD/MBE/SBE PARTICIPATION REGISTRATION:**

OSD/HCPS  
 State of Florida  
 County List:  
 City List:  
 Other List:

**PROGRESS PENDING ISSUES (& RESPONSIBILITIES):**

**Current Critical Issues:**

Issue	Responsibility

**COMMENTS:**  
 Completed under budget.

**PROJECT DIRECTORY:**

**HCPS Department:** Communications & Electronics  
**HCPS Representative:** Jeffrey McNickle

**Contractor / Bid-Vendor:** A-Tech  
**Contractor / Bid-Vendor:** N/A  
**Contractor / Bid-Vendor:** N/A  
**Contractor / Bid-Vendor:** N/A  
**Contractor / Bid-Vendor:** N/A

**Construction Manager / GC:** N/A  
**CM/GC PROJECT MANAGER:** N/A  
**Design Professional:** N/A

**REPORT DATE, PREPARED BY:** 05/01/19-Jeffrey McNickle

**PROJECT DESCRIPTION:**

**Scope of Work:**  
 Replace intercom system.

**CONSTRUCTION UPDATE:**

TYPE	% COMP.	REMARKS
Site	0%	N/A
Finishes	0%	N/A
N/A	0%	N/A
N/A	0%	N/A
N/A	0%	N/A

**CONTRACT STATUS:**

<b>CURRENT CONTRACT AMOUNT:</b>	\$ 150,000.00
<b>AMOUNT BILLED TO DATE:</b>	\$ 140,066.00
<b>PERCENT DOLLARS EXPENDED:</b>	93%
<b>CONTRACT CALENDAR DAYS:</b>	59 Bus Days
<b>CALENDAR DAYS EXPENDED:</b>	59 Bus Days
<b>PERCENT TIME EXPENDED:</b>	100%
<b>TOTAL LOST WEATHER DAYS:</b>	0
